



# OPNFV

## Gambia Retrospective

Please direct any questions  
to [info@opnfv.org](mailto:info@opnfv.org)

# MS1 – project release plans

- Continue to vary widely in quality and content
- Important for identifying accomplishments and features to use to promote the release.
- Several projects making use of suggested release plan template
  - Helpful?



# MS2 – test case database

- Ongoing problems with TC database
  - No longer maintained by Serena
  - Documentation?
  - Status?
  - Who owns?
- Notes
  - Currently restricted to PTL
  - Ownership? Test Working Group.
  - Old documentation is inaccurate.



## Milestone 3 – Installer Integration with OpenStack

- MS3.2 was eliminated and requirements collapsed into MS3.1
  - Helpful?
- We may revert to a single milestone again to simplify release management.

# Milestone 4 – Test Framework Ready

- Issues
  - Not evaluated. Still need better definition.
  - What compliance criteria should be used?
    - Simple assertion?
    - Self test results?
    - Which projects?
- May eliminate for future releases



# Milestone 5 – Scenario Integration and Feature Freeze



- Issues:
  - Scenario status page not consistently updated
    - Need to follow up on previous suggestion to document scenarios in the project info file instead of a wiki page
- Notes
  - Trevor and Sofia express skepticism about using the project file vs. the wiki, i.e., just shifts the location of the documentation without affecting behavior.

# Milestone 6 – Test Case Implementation / Preliminary Documentation

- Issues:
  - Failed to validate preliminary documentation, which led to disruption and delay with the final documentation. This emphasizes the importance of this milestone.



## Milestone 7 – Stable Branch window closed

- Eliminated stable branch window. Simply used MS7 as “complete by” date.
  - Helpful?
- Notes:
  - Consider having LF release engineering implement stable branch for all projects.





## Milestone 9- documentation

- Sub-modules eliminated.
- Delay due to failure to verify prelim documentation at MS6




## Milestone 10 – JIRA issues updated

- Continue to have only fair compliance.
  - Many issues still retain old releases in the “fix version” field



# Milestone 11 - Tagging

- New automation used for tagging in Fraser.
- Helpful?

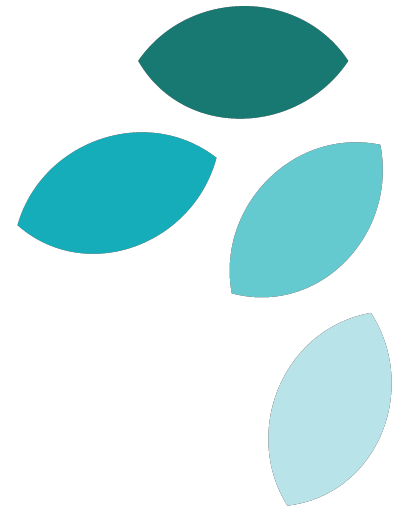

# Other Issues

- Release Plan Evolution
  - Still struggling to develop the new continuous release process
  - Release Process WG meeting regularly
- Changes in release management resources
  - This will necessarily drive process simplification
  - May require more reliance on participants to drive the process





## Questions?

Please direct any questions or comments to  
[info@opnfv.org](mailto:info@opnfv.org)
